



RFP 24-01
PROPOSED PROJECT SCHEDULE

ID	Task Mode	Task Name	Duration	Start	Finish	M	J	Half 2, 2023	J	A	S	O	N	D
1	✓	Contracting Strategy and Calista Agreements Finalized	1 day	Mon 1/15/24	Mon 1/15/24									
2	✓	Permitting	410 days	Tue 1/16/24	Fri 2/14/25									
3	✓	Environmental Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									
4	✓	Environmental Assessment/Draft FNSI	365 days	Wed 2/28/24	Fri 2/14/25									
5	✓	U.S. Army Corps of Engineers Permit	288 days	Wed 2/28/24	Fri 11/29/24									
6	✓	U.S. Fish and Wildlife Service Permit	300 days	Wed 2/28/24	Sat 12/14/24									
7	✓	National Marine Fisheries Service Permit	224 days	Wed 2/28/24	Tue 10/1/24									
8	✓	U.S. Coast Guard Permit	112 days	Wed 2/28/24	Sat 5/15/24									
9	✓	Alaska Department of Natural Resources Permit	300 days	Wed 2/28/24	Sat 12/14/24									
10	✓	Alaska Office of History and Archaeology Permit	287 days	Wed 2/28/24	Sun 12/1/24									
11	✓	Department of Transportation and Public Facilities Permit	308 days	Wed 2/28/24	Sat 12/21/24									
12	✓	Alaska Department of Fish and Game Permit	84 days	Wed 2/28/24	Sun 5/19/24									
13	✓	Municipal, Borough, and Private Approvals/Permits	287 days	Wed 2/28/24	Tue 11/12/24									
14	✓	Engineering	345 days	Tue 1/16/24	Sat 12/14/24									
15	✓	Comm Hut	184 days	Tue 1/16/24	Thu 7/11/24									
16	✓	Engineering Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									
17	✓	Initial Design and Engineering	60 days	Wed 2/28/24	Fri 4/26/24									
18	✓	ACS Review/Comment @30-60% Design	21 days	Fri 4/26/24	Thu 5/16/24									
19	✓	Final Design and Engineering	30 days	Thu 5/16/24	Fri 6/14/24									
20	✓	Final ACS Review/Comment	14 days	Fri 6/14/24	Fri 6/28/24									
21	✓	Design and Engineering Complete	14 days	Fri 6/28/24	Thu 7/11/24									
22	✓	Terrestrial Fiber (Yukon River to Kuskokwim)	345 days	Tue 1/16/24	Sat 12/14/24									
23	✓	Engineering Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									
24	✓	Field Data Collection	300 days	Wed 2/28/24	Sat 12/14/24									
25	✓	Initial Design and Engineering	180 days	Wed 2/28/24	Tue 8/20/24									
26	✓	ACS Review/Comment @30-60% Design	21 days	Tue 8/20/24	Mon 9/9/24									
27	✓	Final Design and Engineering	30 days	Mon 9/9/24	Tue 10/8/24									
28	✓	Final ACS Review/Comment	14 days	Tue 10/8/24	Mon 10/21/24									
29	✓	Design and Engineering Complete	14 days	Tue 10/22/24	Mon 11/4/24									
30	✓	River Fiber Yukon	202 days	Tue 1/16/24	Sun 7/28/24									
31	✓	Engineering Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									

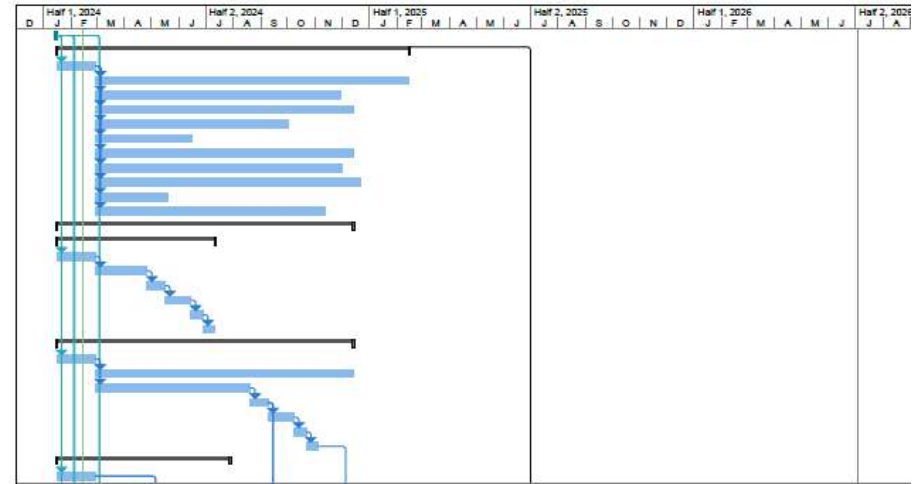

ID	Task Mode	Task Name	Duration	Start	Finish	M	J	Half 2, 2023	J	A	S	O	N	D
32	✓	Field Data Collection	45 days	Mon 5/6/24	Tue 6/18/24									
33	✓	Initial Design and Engineering	45 days	Mon 5/6/24	Tue 6/18/24									
34	✓	ACS Review/Comment @30-60% Design	14 days	Tue 6/18/24	Mon 7/1/24									
35	✓	Final Design and Engineering	14 days	Tue 7/2/24	Mon 7/15/24									
36	✓	Final ACS Review/Comment	7 days	Mon 7/15/24	Mon 7/22/24									
37	✓	Design and Engineering Complete	7 days	Mon 7/22/24	Sun 7/28/24									
38	✓	River Fiber Kuskokwim	259 days	Sun 4/7/24	Fri 12/13/24									
39	✓	Field Data Collection	90 days	Mon 5/6/24	Wed 7/31/24									
40	✓	Initial Design and Engineering	180 days	Sun 4/7/24	Fri 9/27/24									
41	✓	ACS Review/Comment @30-60% Design	21 days	Sat 9/28/24	Fri 10/18/24									
42	✓	Final Design and Engineering	30 days	Fri 10/18/24	Sat 11/16/24									
43	✓	Final ACS Review/Comment	14 days	Sat 11/16/24	Fri 11/29/24									
44	✓	Design and Engineering Complete	14 days	Fri 11/29/24	Fri 12/13/24									
45	✓	Terrestrial Fiber (Aerial Bethel to Napakiak)	215 days	Tue 1/16/24	Sat 8/10/24									
46	✓	Engineering Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									
47	✓	Field Data Collection	106 days	Wed 2/28/24	Sun 6/9/24									
48	✓	Initial Design and Engineering	120 days	Wed 2/28/24	Sun 5/23/24									
49	✓	ACS Review/Comment @30-60% Design	20 days	Sun 6/23/24	Fri 7/12/24									
50	✓	Final Design and Engineering	15 days	Fri 7/12/24	Sat 7/27/24									
51	✓	Final ACS Review/Comment	5 days	Sat 7/27/24	Wed 7/31/24									
52	✓	Design and Engineering Complete	10 days	Thu 8/1/24	Sat 8/10/24									
53	✓	FTTH	235 days	Tue 1/16/24	Tue 9/18/24									
54	✓	Engineering Contractor Acquired	45 days	Tue 1/16/24	Wed 2/28/24									
55	✓	Field Data Collection	60 days	Mon 5/6/24	Tue 7/2/24									
56	✓	Initial Design and Engineering	90 days	Mon 5/6/24	Wed 7/31/24									
57	✓	ACS Review/Comment @30-60% Design	20 days	Thu 8/1/24	Tue 8/20/24									
58	✓	Final Design and Engineering	15 days	Tue 8/20/24	Tue 9/3/24									
59	✓	Final ACS Review/Comment	5 days	Tue 9/3/24	Sun 9/9/24									
60	✓	Design and Engineering Complete	10 days	Sun 9/9/24	Wed 9/18/24									
61	✓	Construction	728.88 days	Sun 2/4/24	Wed 1/7/26									

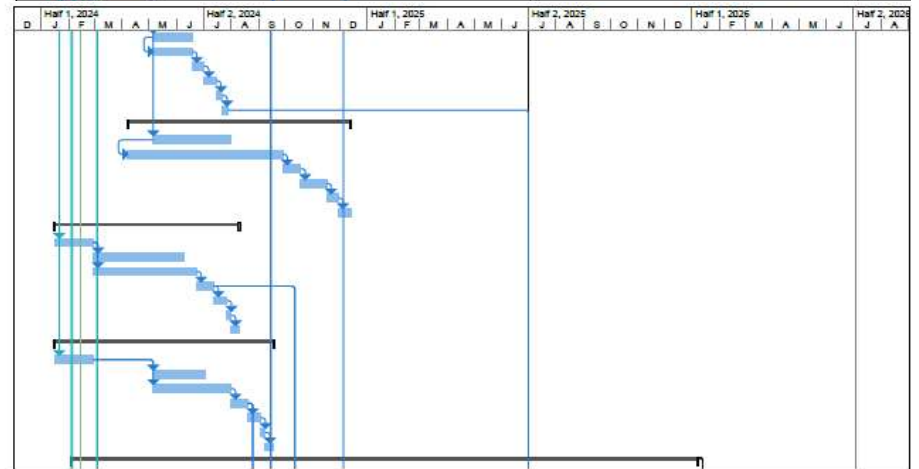

ID	Task Mode	Task Name	Duration	Start	Finish	M	J	Half 2, 2023	J	A	S	O	N	D
62	✓	Terrestrial Yukon to Kuskokwim Fiber Implementation	157 days	Mon 9/9/24	Sat 2/8/25									
63	✓	Implementation Contractor(s) Acquired	30 days	Mon 9/9/24	Tue 10/8/24									
64	✓	Long Lead Material Procurement	90 days	Mon 9/9/24	Thu 12/5/24									
65	✓	Mobilization	30 days	Thu 12/5/24	Fri 1/3/25									
66	✓	Install Fiber Yukon - Kuskokwim	30 days	Fri 1/3/25	Sat 2/1/25									
67	✓	OTDR Test Terrestrial Fiber	4 days	Sat 2/1/25	Wed 2/6/25									
68	✓	Demobe/Cleanup	3 days	Wed 2/6/25	Sat 2/8/25									
69	✓	River Fiber Implementation Yukon	688.26 days	Mon 2/6/24	Sun 7/27/26									
70	✓	Implementation Contractor(s) Acquired	60 days	Mon 2/5/24	Tue 4/2/24									
71	✓	Long Lead Material Procurement (Fiber)	180 days	Wed 4/3/24	Mon 9/23/24									
72	✓	Long Lead Material Procurement (Electronics)	180 days	Wed 4/3/24	Mon 9/23/24									
73	✓	Segment 1 Complete	90 days	Mon 5/10/24	Wed 9/4/24									
74	✓	Upstream Yukon Mobilization	5 days	Tue 7/1/25	Sat 7/5/25									
75	✓	Holy Cross Directional Drilling/Beach Manhole	5 days	Sat 7/5/25	Thu 7/10/25									
76	✓	Holy Cross to Landfill at Winter Trail	5 days	Sat 7/18/25	Sun 7/13/25									
77	✓	Winter Trail Directional Drilling/Beach Manhole	5 days	Sun 7/13/25	Fri 7/18/25									

